## CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR FLOOD CONTROL PROJECTS

1. Project Name: Kaunakakai Stream FCP

2. Date of Inspection: October 30, 2002

### 3a. Inspection Personnel:

<u>Name</u>		Agency/Office	Telephone No.
a.	Dan Meyers	COE	438-8875
b.	Rick Oleniacz	COE	438-1981
c.	Maj. Scott Schriner	COE (CEPOH-DD)	438-1091
d.	Isaacs Kan Hai	Maui County/DPW	553-3221

# 3b. Accompanying Personnel:

	<u>Name</u>	Agency/Office	Telephone No.
1.	Miles Takayesu	COE (CEPOH-RE)	438-1981

## 4. Discussion:

The project: On previous inspections it was noted that the crest of the levee's left bank, below the main highway, has continued to erode. The erosion is probably due to recreational vehicles and aggravated by unusually dry weather conditions. Mr. Arce's initiative to add armor stone protection (#25 - #500) to the levee's sideslope from Sta. (-)4+00 - Sta. 9+50 has been completed. The estimated value of the armor stone protection is approximately \$120,000.00. Mr. Arce is commended for his initiative and efforts in this matter. Only minor deficiencies were noted and are listed below for corrective action:



a. Sta. 10+20, Left Bank (LB), remove stockpile of excavated material from levee crest and sideslope.



b. Sta. 13+00, Left Bank (LB), remove woody vegetation from levee sideslope.



c. Sta. 23+00, LB, remove juvenile tree from the townside sideslope of the levee.




d. Sta. 30+00, LB, restore maintenance access road.



e. Sta. 25+00, Right Bank, (RB), remove woody vegetation from townside sideslope of the levee.




f. Sta. 20+00, RB side, clear culvert opening.

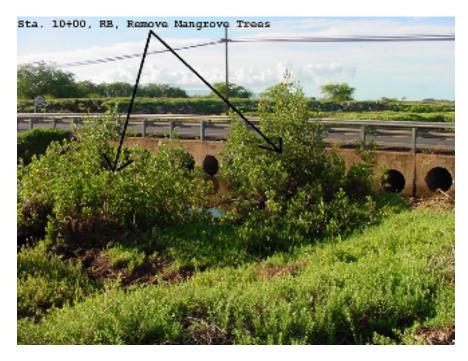

g. Sta. 10+00, RB, remove mangrove trees from toe of levee.



h. Sta. 8+00, LB, remove vegetation from levee.

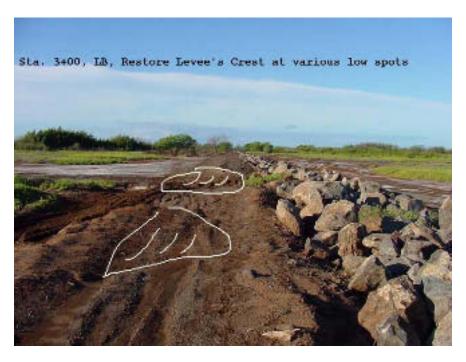

i. Sta. 3+00, LB, fill eroded areas restoring levee crest.

## 5. Findings/Conclusions:

IAW ER 500-1-1, ( dtd 30 September 2001 ), and based on this CEI, the Project Condition Code is ACCEPTABLE and the project is considered ACTIVE in the Rehabilitation and Inspection Program.

Dan Mey	rers, CEPC	H-EC-T	

Signed: \_\_\_\_\_

Enclosure(s)

- 1. Misc. Photos
- 2. Site Plan



Sta. 12+00, Centerline of project.



Sta. 14+00, Overview of project.



Upper Limit of LB, Levee



Sta. 19+00, Access Steps
