



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT**FOR HURRICANE & SHORE PROTECTION PROJECTS****Honolulu Engineer District****CEPOH-EC-T**

Saipan05rpt-spp.doc

1. Project Name: Saipan Beach Road SPP

2. Date of Inspection: February 7, 2005

3. Inspection Personnel:

Name	Agency/Office	Telephone No.
a. Dan Meyers	CEPOH-EC-T	808-438-8875
b. Joel Hendrix	CEPOH-EM	808-438-1275
c. Mr. Henry Bautista	DPW	670-322-9436
d. Mr. Rosel R. Torres	DPW	670-322-9828

4. Discussion:

The project provides for approximately 1,000 LF of beach sand fill and plant stabilization. Crest elevation of +10 feet MLLW with a slope of 1V on 1.5 H . It was noted that the project has been modified. The modification consisted of placing a concrete walkway on top of the beach sand fill. The walkway is not part of this project and is not eligible for rehabilitation under PL84-99. Station numbers should be established along the walkway to facilitate future inspections. The discrepancies listed below were noted and suggestions were made to the DPW representatives.

5. Rating for FY05

Project Rating: "S, **Satisfactory**"

Project Condition Code: "A, **Acceptable**"

Project Status: "**Active**"



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



- a. Sta. 0+00, Overview facing North, no action required (sand fill begins at Sta. 2+00 \pm).



- b. Sta. 1+00, no action required.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



c. Sta. 2+00, no action required.



d. Sta. 2+80, 24" culvert.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



- e. Sta. 4+00, overview facing north, replenish eroded sand fill as needed.



- f. Sta. 5+00, overview facing north. replenish eroded sand fill.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



g. Sta. 6+00, Replenish eroded sand fill as needed.



h. Sta. 7+00, no action required.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



- i. Sta. 8+00, replenish sand fill as needed.



- j. Sta. 9+00.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



k. Sta. 10+00, Reference Photo.



l. Sta. 10+33, Walkway begins to slope, re-grade sand fill during walkway repairs.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc



- m. Sta. 11+00, Sta. 10+33, Walkway begins to slope, re-grade sand fill during walkway repairs.



- n. Sta. 12+00



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan05rpt-spp.doc



- o. Sta. 12+80, End of Project



- p. Reference Photo (Sta. 14+48, Centerline of 24" culvert).



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT**FOR HURRICANE & SHORE PROTECTION PROJECTS****Honolulu Engineer District****CEPOH-EC-T**

*Saipan05rpt-spp.doc***6. Findings/Conclusions:**

IAW ER 500-1-1, (dtd 30 September 2001), and based on this CEI, the Project is rated SATISFACTORY , Project Condition Code is ACCEPTABLE and the project is considered ACTIVE in the Rehabilitation and Inspection Program.

Signed: _____
Dan Meyers, CEPOH-EC-T

Signed: _____
James Pennaz, P.E.,CH, CEPOH-EC-T

Enclosure(s)

1. Site Plan


CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan05rpt-spp.doc

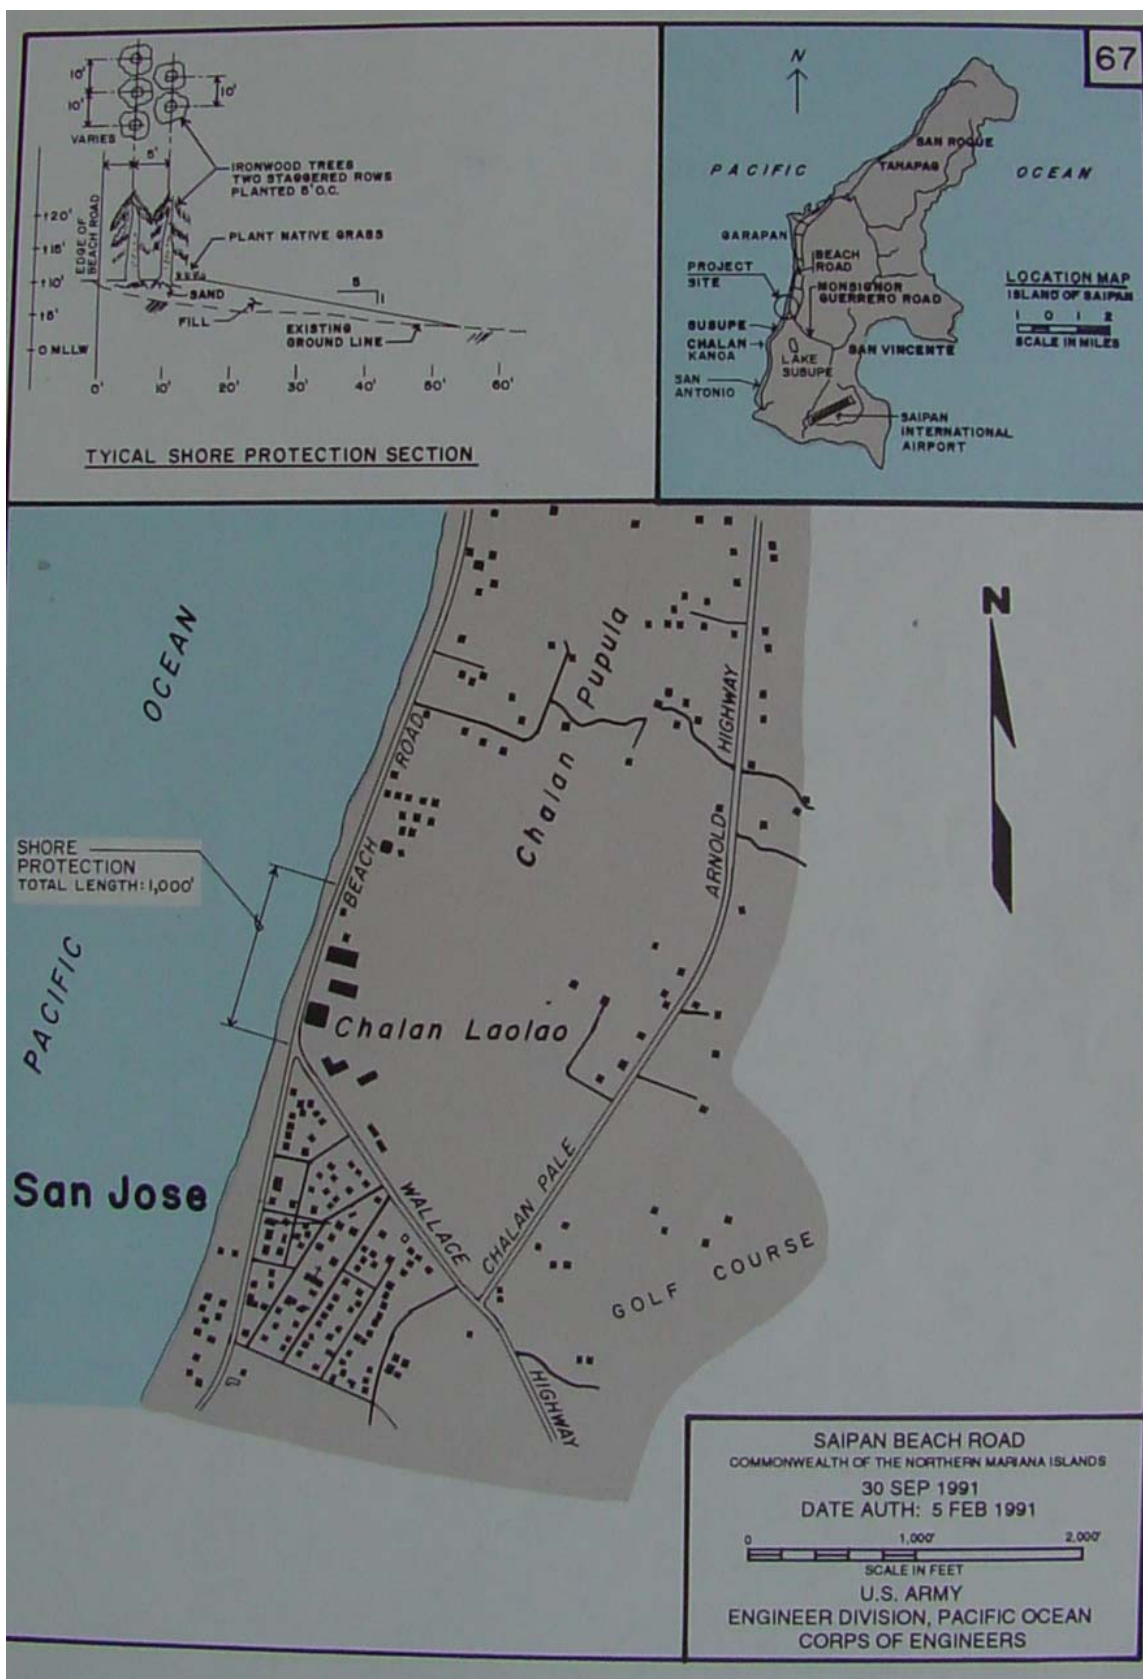



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan05rpt-spp.doc

SAIPAN BEACH ROAD, NORTHERN MARIANAS

CONDITION OF IMPROVEMENT 30 SEPTEMBER 1993

PREVIOUS PROJECTS: None.

EXISTING PROJECT: Authorized for construction on 5 February 1991 under Section 14 of the Flood Control Act of 1946, as amended. Provides for 1,000 feet of beach sand fill and plant stabilization.

PROGRESS OF WORK

Completed and Under Maintenance: A construction contract awarded in Aug 1991 was completed in April 1992 for \$93,400.

Work Remaining: None.

COST OF CONSTRUCTION:

	<u>New Work</u>
United States Funds	<u>\$156,000</u>
Total Costs	\$156,000




CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan05rpt-spp.doc

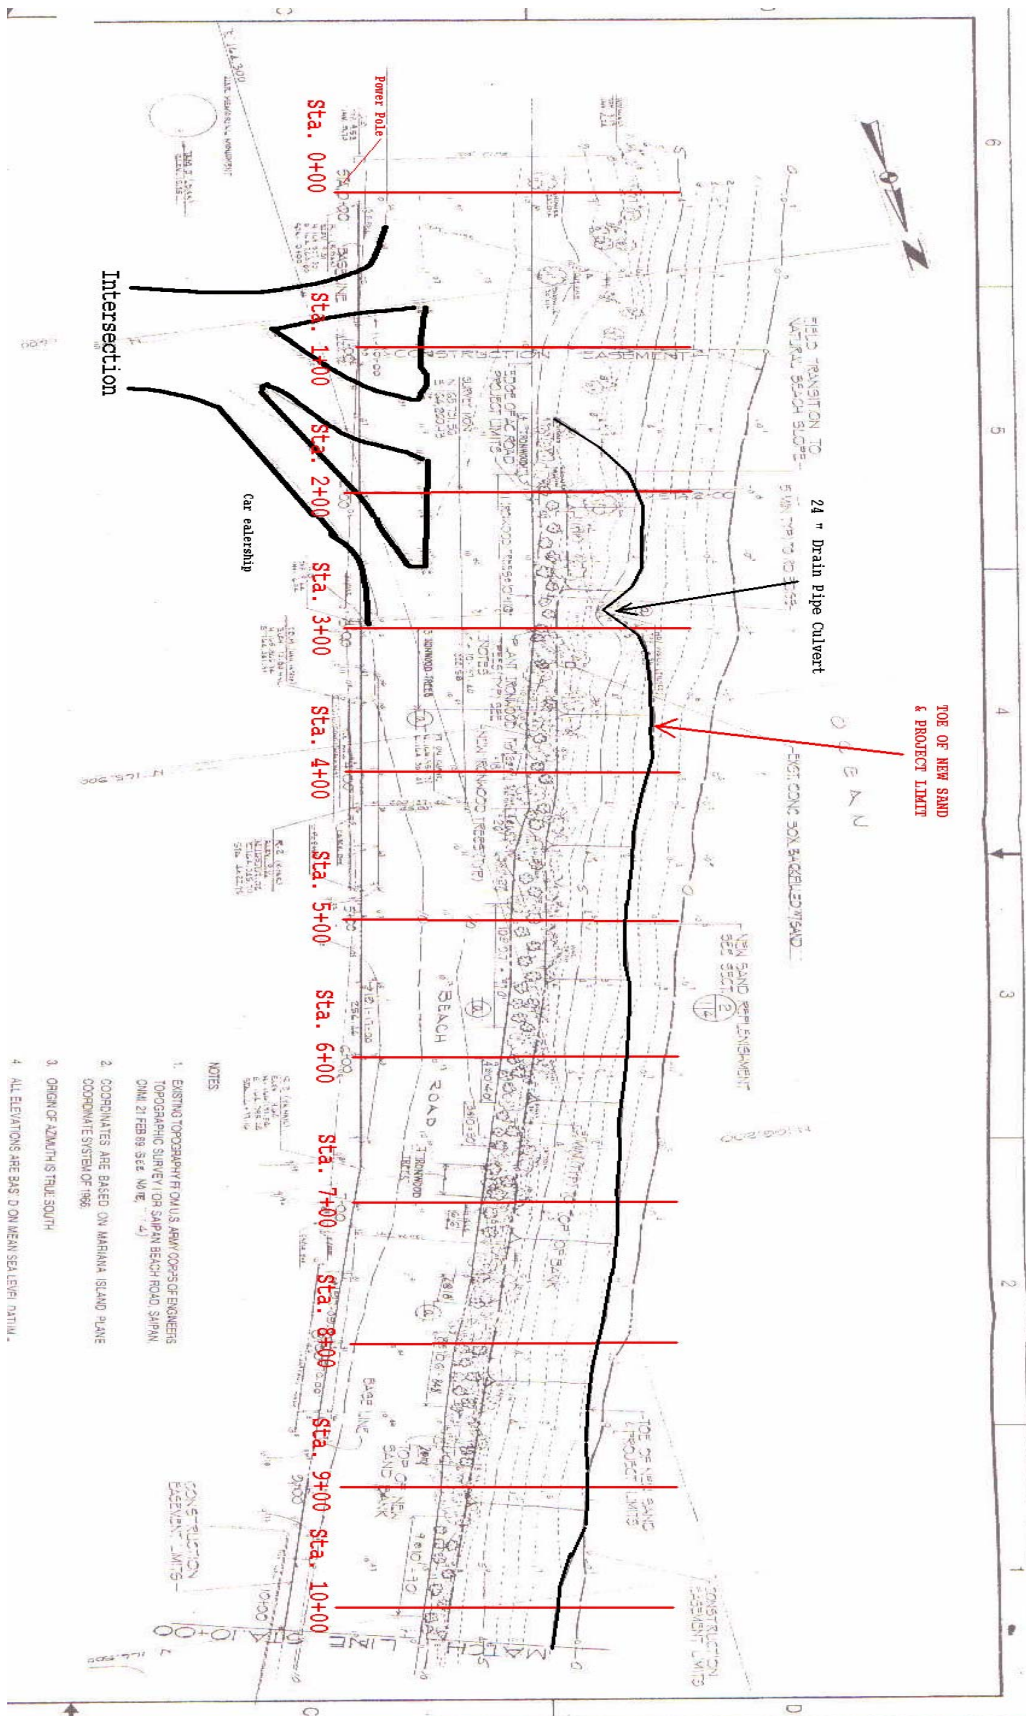




CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District
CEPOH-EC-T

Saipan05rpt-spp.doc

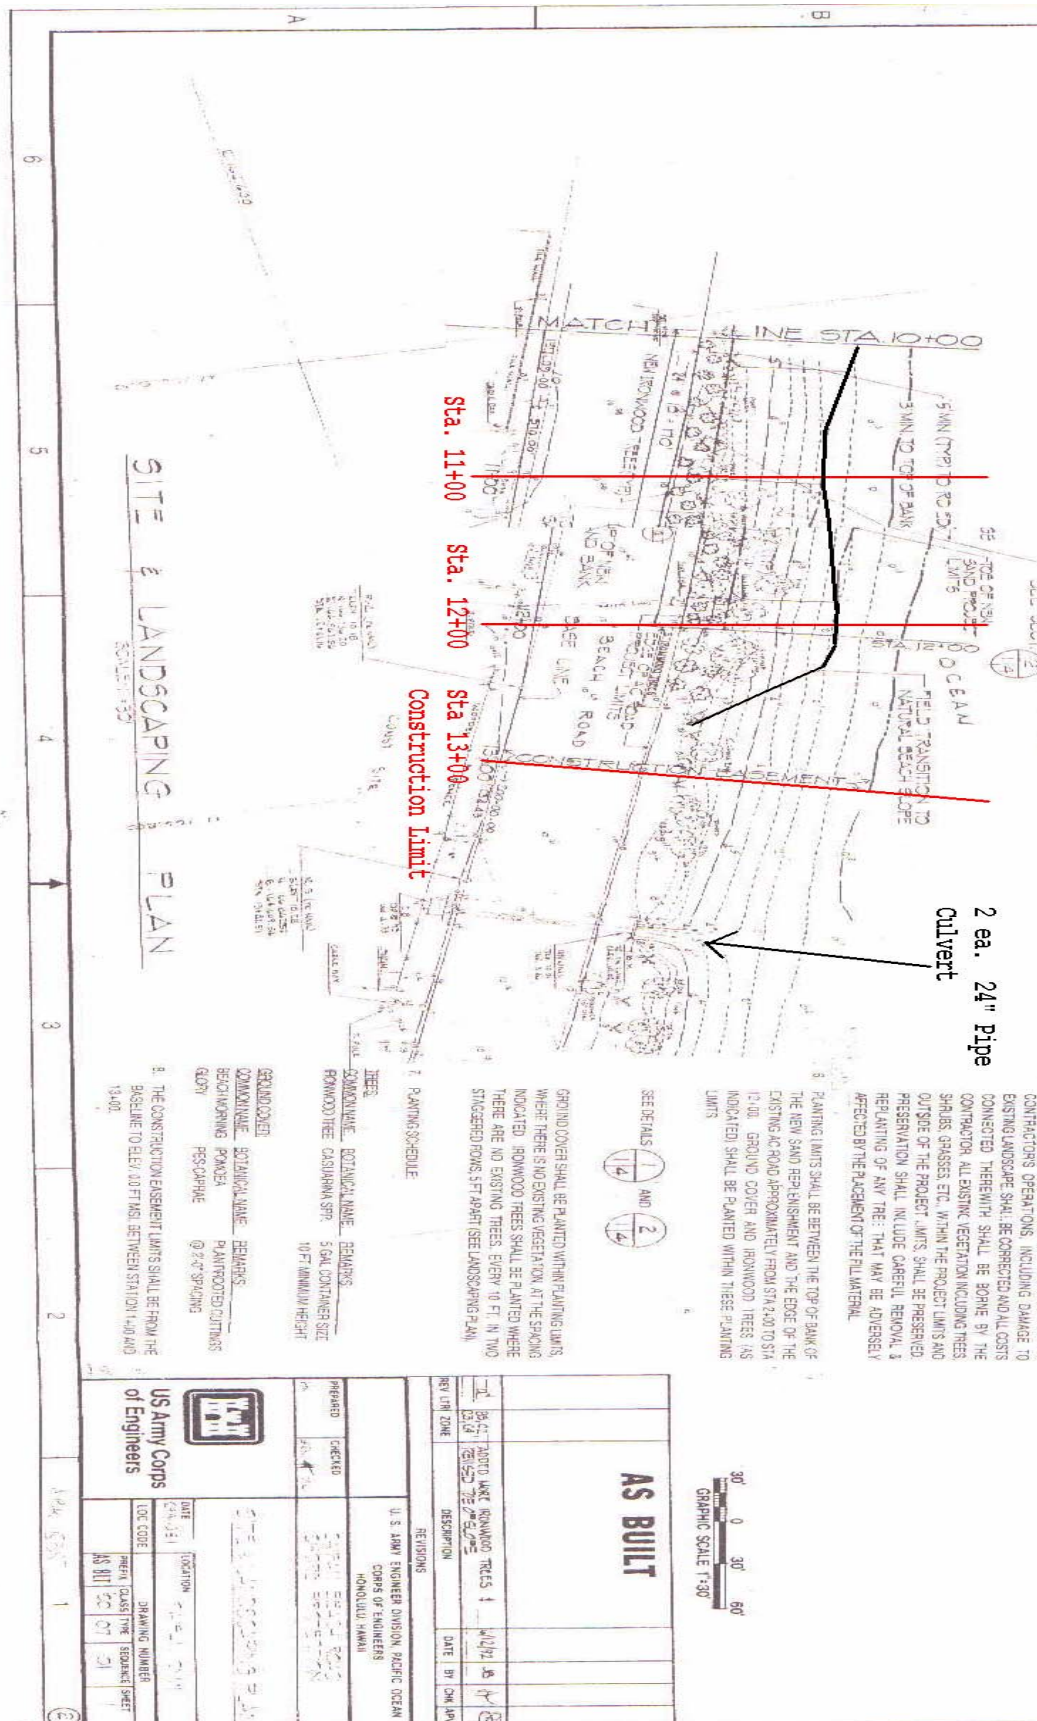

**CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT**

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan05rpt-spp.doc

Saipan Beach Road Project (Road Elevations):

Station #	Mauka Edge of Road	Center Line Road	Makai Edge of Road	
2+00	11.20	10.91	10.19	(south end of the project)
3+00	10.15	10.61	10.01	
4+00	9.90	10.12	9.86	
5+00	9.72	10.17	9.75	
6+00	9.63	10.23	9.78	
7+00	9.60	10.37	10.07	
8+00	9.87	10.41	10.08	
9+00	9.97	10.49	10.30	
10+00	9.97	10.48	10.11	
11+00	10.16	10.62	10.15	
12+00	10.18	10.61	10.31	(north end of the project)
