CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

- 1. Project Name: Matafao Shore Protection Project
- 2. Date of Inspection: April 10, 2002

3. Inspection Personnel:

Name		Agency/Office	Telephone No.	
a.	Dan Meyers	COE	438-8875	
b.	Joel Hendrix	COE	438-1275	
c.	Rick Oleniacz	COE	438-1981	
d.	Mikaele Senid	DPW	633-4141	

4. CEI Rating:

Due to the lack of vegetation control a thorough inspection could not be conducted. In accordance with ER 500-1-1, (dtd 30 September 2001), and based on this CEI, the Project is rated MARGINALLY SATISIFACTORY, Project Condition Code is MINIMALLY ACCEPTABLE and the project is considered ACTIVE in the Rehabilitation and Inspection Program. This project will be re-evaluated in September 2002.

5. Discussion:

The SPP is 405LF. Sta. 1+55 is the beginning of the structure, located at the East-End of the project, the entrance road to the school is at Sta. 1+55 and ends at Sta. 5+60. All discrepancies were noted and brought to the representative's attention. The major deficiencies were as follows:



a. Sta. 2+55, Remove vines from crest of the structure.




b. Sta. 4+05, Remove vines and trees from revetment, unable to inspect.

c. Sta. 4+10, 1 cracked armor stone midway down the sideslope, no problems noted.



d. Sta. 3+80 TO Sta. 4+30, Remove vegetation (vines & ferns) from crest of revetment, unable to inspect.

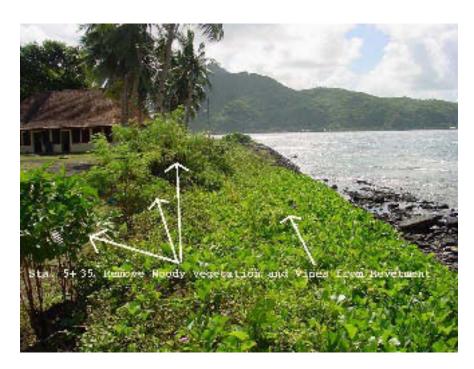

e. Sta. 5+35, Remove woody vegetation and vines from revetment, unable to inspect.



f. Sta. 5+60, Remove woody vegetation and vines from revetment, unable to inspect.

6. Notes / Recommendations:

The focus of the maintenance required should be directed at vegetation control. Removal or herbicides are recommended in lieu of cutting.

Signed:				
Dai	n Meyers,	CEPO	H-EC	-T
Signed:				
т:,	n Donnag	ים מ	Ch	$CEDOU_EC_T$

Attached: Additional Photo Photos Sheet Project Index Map



Adjacent too and East of Existing Project, Note New School Building in the background.

