



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan03rpt-spp.doc

1. Project Name: Saipan Beach Road SPP
2. Date of Inspection: July 9, 2003
3. Inspection Personnel:

Name	Agency/Office	Telephone No.
a. Dan Meyers	CEPOH-EC-T	808-438-8875
b. Rick Olenicaz	CEPOH-EM	808-438-1981
c. Joel Hendrix	CEPOH-EM	808-438-1275
c. Mr. Roy Reyes	DPW	670-322-9828

4. Discussion:

The project provides for approximately 1,000 LF of beach sand fill and plant stabilization. Crest elevation of +10 feet MLLW with a slope of 1V on 1.5 H . It was noted that the project has been modified. The modification consisted of placing a concrete walkway on top of the beach sand fill. The walkway is not part of this project and is not eligible for rehabilitation under PL84-99. **The Project is rated MARGINALLY SATISFACTORY and is ACCEPTABLE.** The discrepancies listed below were noted and suggestions were made to the DPW representatives.



- a. Sta. 0+00, Overview facing North, no action required.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan03rpt-spp.doc



b. Sta. 1+00, replenish eroded sand fill.



c. Sta. 2+50, replenish eroded sand fill.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan03rpt-spp.doc



d. Sta. 3+50, replenish eroded sand fill.



e. Sta. 4+00, overview facing north, replenish eroded sand fill.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT
FOR HURRICANE & SHORE PROTECTION PROJECTS
Honolulu Engineer District
CEPOH-EC-T

Saipan03rpt-spp.doc



f. Sta. 6+00, overview facing east. Replenish eroded sand fill.



g. Sta. 8+00, walkway rest area cut into project. Replenish eroded sand fill.



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan03rpt-spp.doc



h. Sta. 10+00, replenish eroded sand fill.

5. Findings/Conclusions:

IAW ER 500-1-1, (dtd 30 September 2001), and based on this CEI, the Project is rated **MARGINALLY SATISFACTORY** , Project Condition Code is **ACCEPTABLE** and the project is considered **ACTIVE** in the Rehabilitation and Inspection Program.

Signed: _____

Dan Meyers, CEPOH-EC-T

Signed: _____

James Pennaz, P.E.,CH, CEPOH-EC-T

Enclosure(s)

1. Site Plan


CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan03rpt-spp.doc

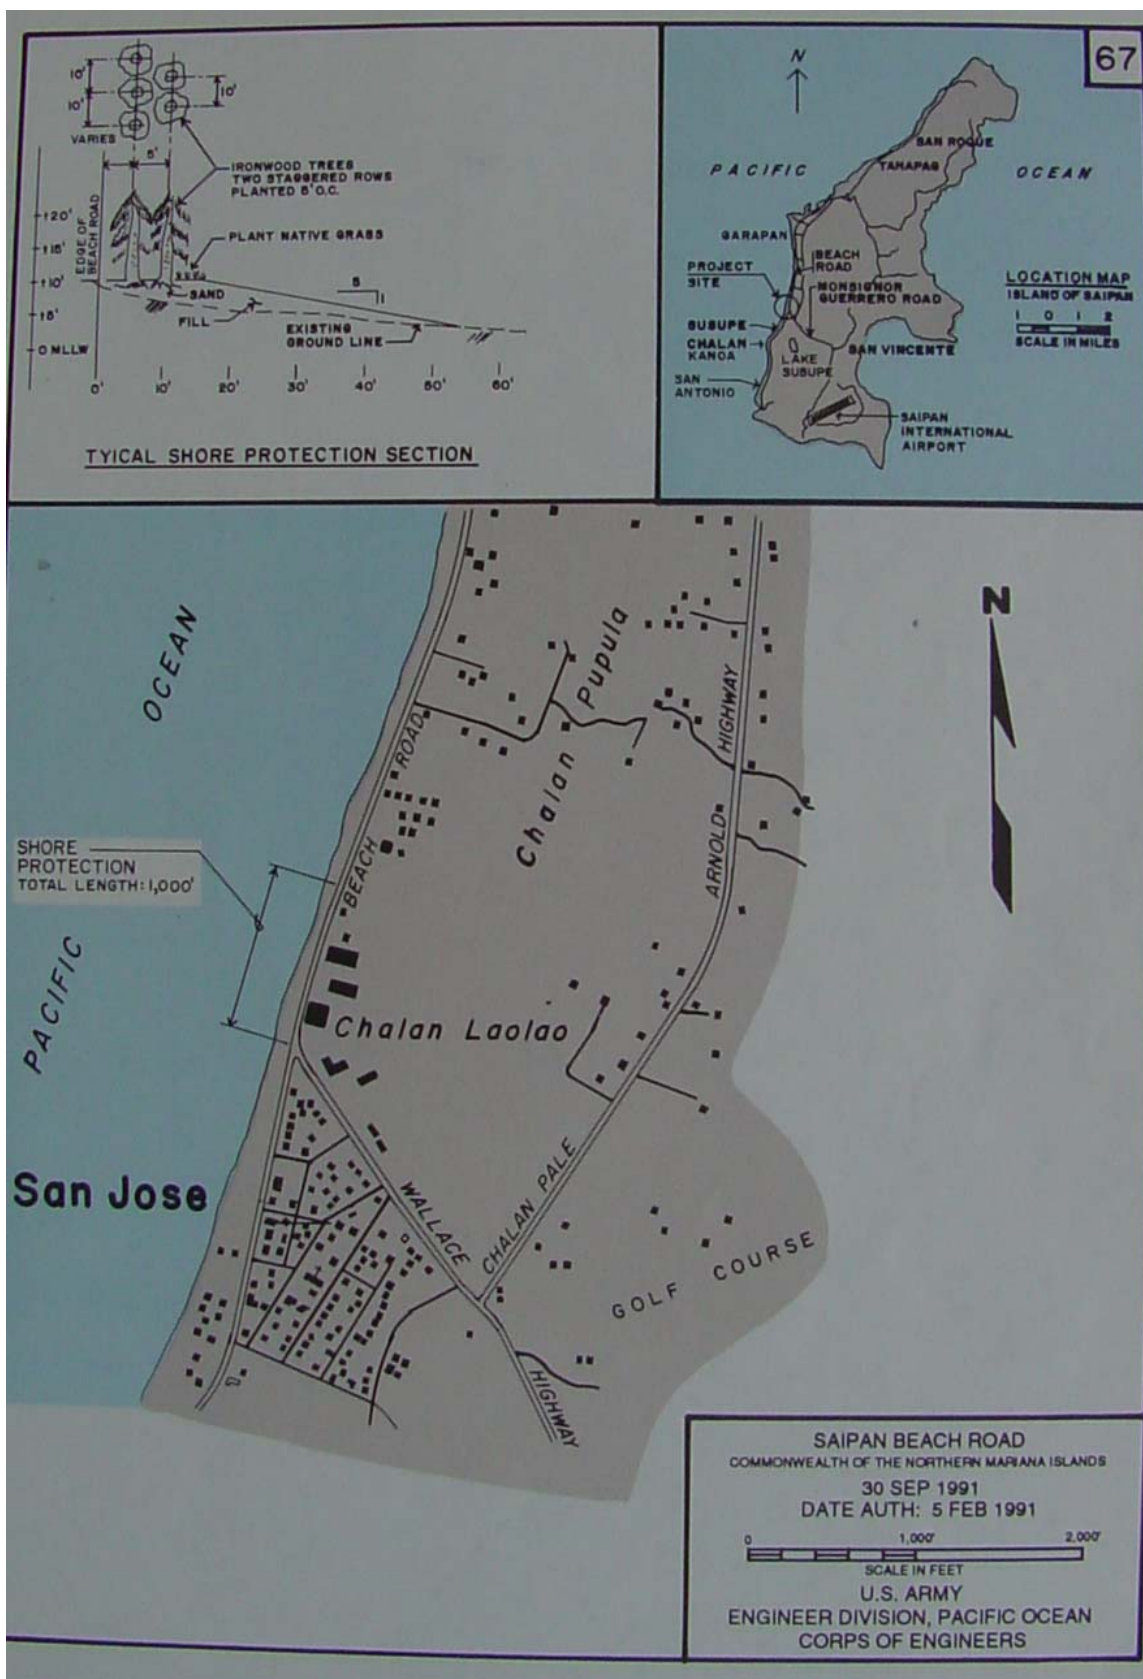



CONTINUING ELIGIBILITY INSPECTION (CEI) REPORT

FOR HURRICANE & SHORE PROTECTION PROJECTS

Honolulu Engineer District

CEPOH-EC-T

Saipan03rpt-spp.doc

SAIPAN BEACH ROAD, NORTHERN MARIANAS

CONDITION OF IMPROVEMENT 30 SEPTEMBER 1993

PREVIOUS PROJECTS: None.

EXISTING PROJECT: Authorized for construction on 5 February 1991 under Section 14 of the Flood Control Act of 1946, as amended. Provides for 1,000 feet of beach sand fill and plant stabilization.

PROGRESS OF WORK

Completed and Under Maintenance: A construction contract awarded in Aug 1991 was completed in April 1992 for \$93,400.

Work Remaining: None.

COST OF CONSTRUCTION:

	<u>New Work</u>
United States Funds	<u>\$156,000</u>
Total Costs	\$156,000
